


### かながわ環境整備センター埋立量の推移

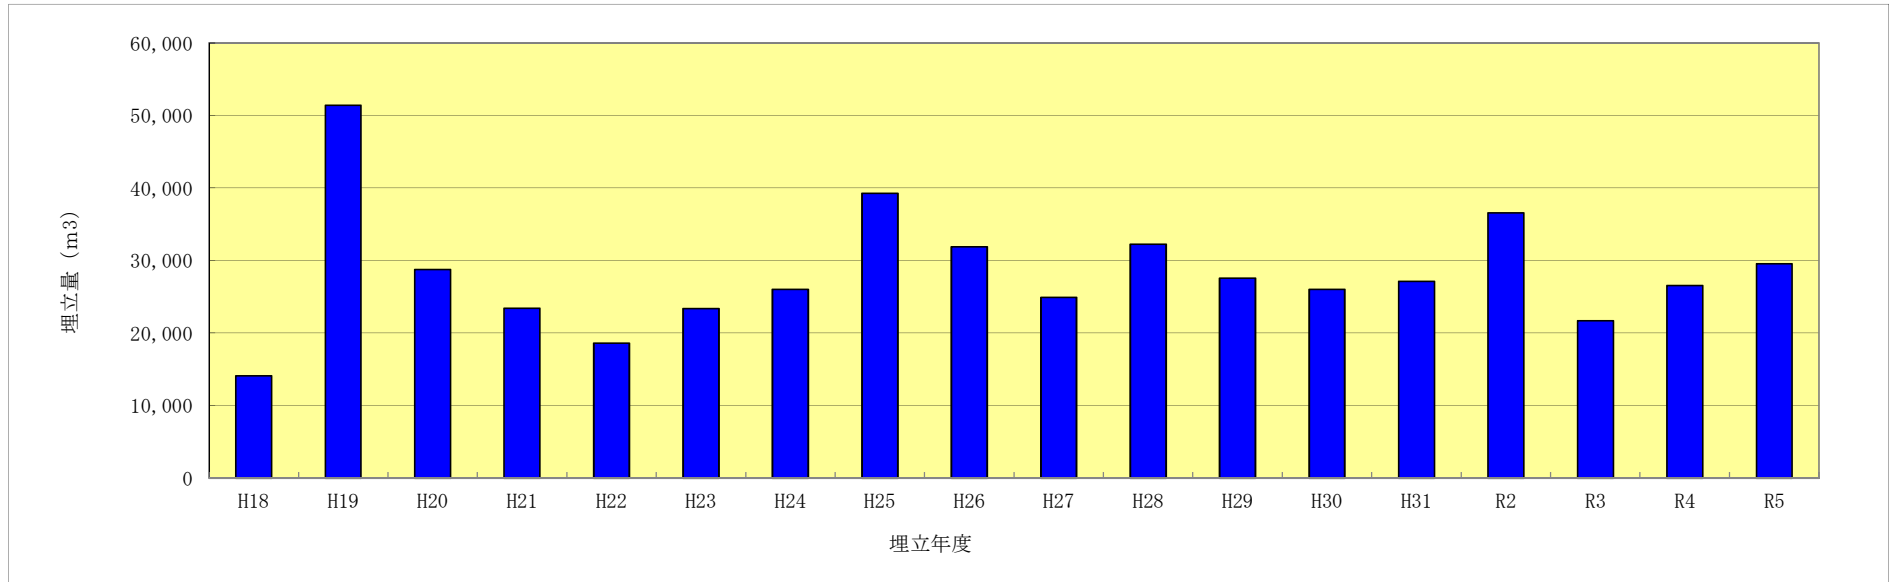

|              | H18    | H19    | H20    | H21    | H22    | H23    | H24    | H25    | H26    | H27    | H28    | H29    | H30    | H31    | R2     | R3     | R4     | R5     | 合計      |
|--------------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|---------|
| 廃棄物 (m³)     | 10,176 | 42,767 | 23,185 | 19,506 | 13,440 | 16,237 | 21,152 | 31,675 | 24,898 | 18,478 | 23,136 | 22,634 | 20,295 | 19,368 | 29,468 | 14,840 | 20,260 | 23,440 | 394,955 |
| 覆土 (m³)      | 3,913  | 8,639  | 5,550  | 3,901  | 5,167  | 7,146  | 4,865  | 7,565  | 6,974  | 6,430  | 9,117  | 4,912  | 5,698  | 7,761  | 7,087  | 6,855  | 6,267  | 6,125  | 113,972 |
| 埋立量 (m³)     | 14,089 | 51,406 | 28,735 | 23,407 | 18,606 | 23,383 | 26,017 | 39,240 | 31,872 | 24,908 | 32,253 | 27,546 | 25,993 | 27,129 | 36,555 | 21,695 | 26,527 | 29,565 | 508,926 |
| 廃棄物重量 (t)    | 10,503 | 29,567 | 21,132 | 15,922 | 15,190 | 16,619 | 23,591 | 29,894 | 26,100 | 26,033 | 24,432 | 22,211 | 19,271 | 24,437 | 25,051 | 18,095 | 17,702 | 16,487 | 382,237 |
| 廃棄物比重 (t/m³) | 1.03   | 0.69   | 0.91   | 0.82   | 1.13   | 1.02   | 1.12   | 0.94   | 1.05   | 1.41   | 1.06   | 0.98   | 0.95   | 1.26   | 0.85   | 1.22   | 0.87   | 0.70   | 0.97    |
| 埋立量 (%)      | 1.9    | 6.8    | 3.8    | 3.1    | 2.5    | 3.1    | 3.5    | 5.2    | 4.2    | 3.3    | 4.3    | 3.7    | 3.5    | 3.6    | 4.9    | 2.9    | 3.5    | 3.9    |         |
| 埋立進捗率 (%)    | 1.9    | 8.7    | 12.5   | 15.6   | 18.1   | 21.2   | 24.7   | 29.9   | 34.1   | 37.4   | 41.7   | 45.3   | 48.8   | 52.4   | 57.3   | 60.1   | 63.7   | 67.6   |         |

| 許可を得た埋立量  | これまでの埋立量  | 進捗率   |
|-----------|-----------|-------|
| 753,000m³ | 508,926m³ | 67.6% |

(令和6年3月31日現在)
