


かながわ環境整備センター埋立量の推移

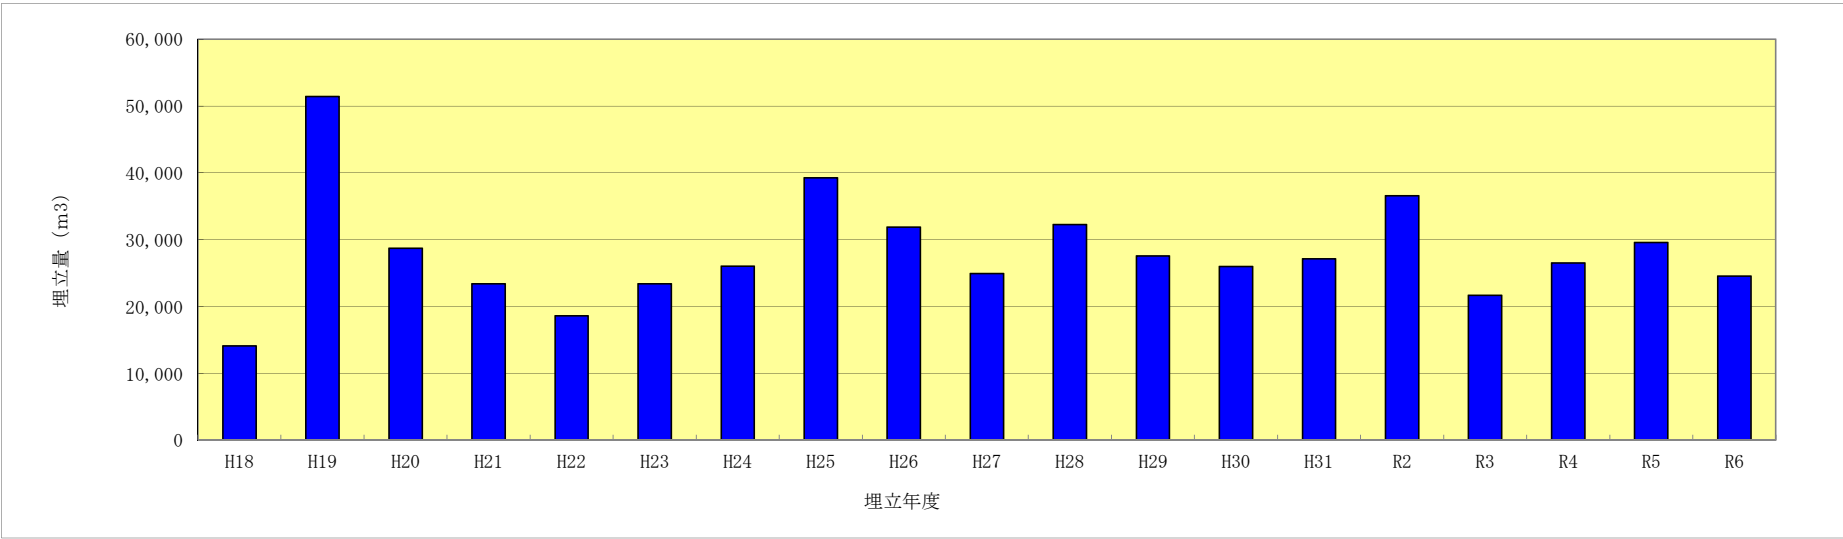

	H18	H19	H20	H21	H22	H23	H24	H25	H26	H27	H28	H29	H30	H31	R2	R3	R4	R5	R6	合計
廃棄物(m³)	10,176	42,767	23,185	19,506	13,440	16,237	21,152	31,675	24,898	18,478	23,136	22,634	20,295	19,368	29,468	14,840	20,260	23,440	16,977	411,932
覆土(m³)	3,913	8,639	5,550	3,901	5,167	7,146	4,865	7,565	6,974	6,430	9,117	4,912	5,698	7,761	7,087	6,855	6,267	6,125	7,576	121,548
埋立量(m³)	14,089	51,406	28,735	23,407	18,606	23,383	26,017	39,240	31,872	24,908	32,253	27,546	25,993	27,129	36,555	21,695	26,527	29,565	24,553	533,480
廃棄物重量 (t)	10,503	29,567	21,132	15,922	15,190	16,619	23,591	29,894	26,100	26,033	24,432	22,211	19,271	24,437	25,051	18,095	17,702	16,487	16,854	399,091
廃棄物比重 (t/m³)	1.03	0.69	0.91	0.82	1.13	1.02	1.12	0.94	1.05	1.41	1.06	0.98	0.95	1.26	0.85	1.22	0.87	0.70	0.99	0.97
埋立量(%)	1.9	6.8	3.8	3.1	2.5	3.1	3.5	5.2	4.2	3.3	4.3	3.7	3.5	3.6	4.9	2.9	3.5	3.9	3.3	
埋立進捗率(%)	1.9	8.7	12.5	15.6	18.1	21.2	24.7	29.9	34.1	37.4	41.7	45.3	48.8	52.4	57.3	60.1	63.7	67.6	70.9	

許可を得た埋立量	これまでの埋立量	進捗率
753,000m³	533,480m³	70.9%

(令和7年3月31日現在)
